BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Comprehensive Development of Roads and Drains at Kaveri Layout, AMS Layout, Aditya Nagara 1st and 2nd stage Doddabettahalli, Yelahanka 4th Phase and Muneshwara Layout and Surrounding Areas in Ward No:63 of Yelahanka Division (Package No 12)
Consultants	:	Civil Pro
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	12-08-21
Project End Date	:	08-02-22
Project Length in Months	:	180 Days

Sl. No	Assignment	Unit	Modified schedule-B Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
1	Earthwork excavation by manual means for roads, drains & similar works in ordinary soil excavated surface levelled and sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods complete as per specifications complete as per specification and directions of the Engineer in charge.	Cum	8411.08	8411.08	100	14-08-21	19-08-21	5
2	Removing and refixing stone slabs of drains and pointing in CM (1:3) complete as per specification and directions of the Engineer in charge.	Cum	1218.60	1218.60	100	13-08-21	16-08-21	3
3	Providing two line dressing to granite stone slab / granite stone masonry as per specifications. KBS 5.1.13 complete as per specification and directions of the Engineer in charge. QTY UPTO 125%	Cum	1218.60	1218.60	100	01-10-21	03-10-21	2
4	Providing and laying Plain cement concrete of mix 1:3:6 with OPC @ 220kgs, with crushed 40mm and down size graded granite metal course aggregates @0.89cum and fine aggregates @ 0.46cum, in foundation mechanically mixed, placed in foundation and compacted by vibration including curing for 14 days including cost of all materials, labour, HOM curing, form works, scaffolding and centering complete as per specification and directions of the Engineer in charge. QTY UPTO 125%	Cum	1842.64	1842.64	100	15-08-21	20-08-21	5
5	Providing laying plain/ reinforced cement concrete for side Drains Using M20 nominal mix Concrete with OPC at 300kgs.With 20mm and Down size granite metal course aggregate at 0.69cum and fine aggregate at 0.43cum Machne mixed, well compacted for wall and Bottom including centering shuttering,cost of materials,HOM of Machinery,Curing Etc.,Complete Excluding cost of Steel as per morth MORTH specification No. 1500, 1700, 2200. Including Cost of material, Labour, HOM complete as per Specification-WALL & Bottom thickness 15Cmcomplete as per specification and directions of the Engineer in charge. QTY UPTO 125%	Cum	2726.35	2726.35	100	19-08-21	03-09-21	15
6	Providing T.M.T bars Fe 500 steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary complete as per design (laps, hooks and wastage shall not be measured and paid) cost of materials, labour, HOM of machinery complete as per specifications. MORTH Specification 1600,1700&2200Specification complete as per specification and directions of the Engineer in charge. QTY UPTO 125%	Tonne	169.98	169.98	100	18-08-21	25-08-21	7

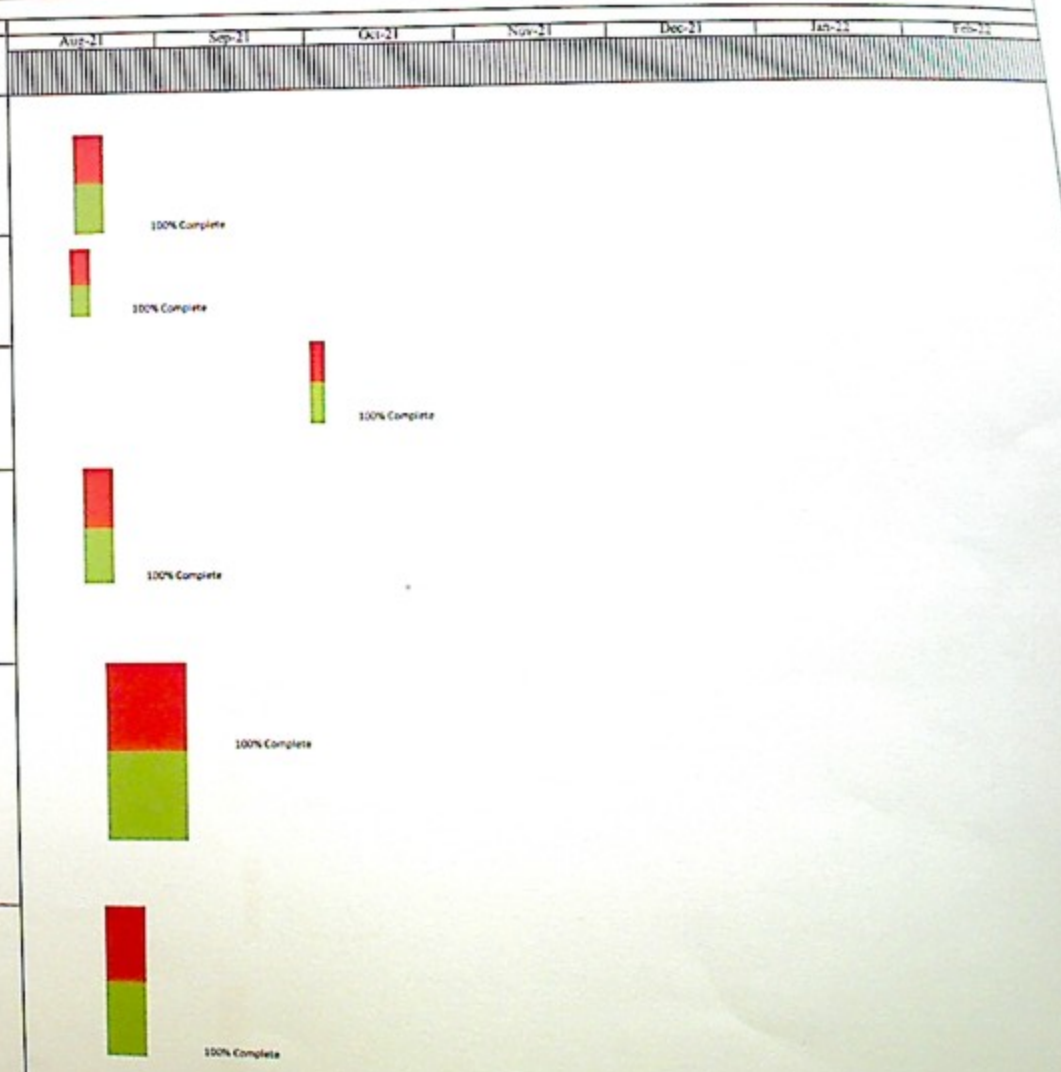

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	: Executive Engineer Yelahanka Division
Project Name	: Comprehensive Development of Roads and Drains at Kaveri Layout, AMS Layout, Aditya Nagara 1st and 2nd stage Doddabettahalli, Yelahanka 4th Phase and Maneshwara Layout and Surrounding Areas in Ward No 93 of Yelahanka Division (Package No 12)
Consultants	: Civil Pro
Project Manager /Team Leader	: Karthik Rechan
Project Start Date	: 12-08-21
Project End Date	: 08-02-22
Project Length in Months	: 180 Days

Sl No	Assignment	Unit	Modified schedule-B Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
7	Providing and Fixing pre cast covering Slab made out of CC 1:2:4 with 10cm thick and Finishing cutting ,including form work,curing,including cost of alll materials, labour,hire charges of machinery,loading,unloading,lead and lift,transportation etc ,copmplete. (Data Rate) complete as per specification and directions of the Engineer in charge. QTY UPTO 125%	Sqm	6114.36	6114.36	100	08-09-21	11-09-21	3
8	Providing and Fixing pre cast covering Slab 250mm thick made out of CC 1:2:4 and jelly 20mm Down size with steel reinforcement including form work,curing,including cost of alll materials, labour,hire charges of machinery, loading, unloading, lead and lift,transportation etc ,complete.As per Engineer incharge QTY UPTO 125%	Sqm	403.47	403.47	100	08-09-21	11-09-21	3
9	Providing and laying in position plain cement concrete of Mix 1:2:4 with OPC @ 240kgs, with 20mm and down size graded granite metal course aggregates @ 0.878 cum and fine aggregtes @ 0.53cum, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation, plinth and cills, including cost of all materials, labour, HOM curing complete as per specification and directions of the Engineer in charge.	Cum	69.12	69.12	100	12-09-21	15-09-21	3
10	Providing and fixing pre cast solid cement concrete kerb stones made out of CC 1:2:4 with top and bottom width 114 and 165 mm respectively, 400mm high and 450mm in length finished with CM 1:3 plastering and finishing cutting including formwork, curing, including cost of materials, labour charges of machinery, loading and unloading, lead and lift, transportation etc.,complete as per specification and directions of the Engineer in charge.	Nos	7681.00	7681.00	100	12-09-21	15-09-21	3
11	Painting two coats after filling the surface with synthetic enamel paint in approved shades on new plastered concrete surfaces, with materials, labour complete as per specifications. MORTH Chapter 8 complete as per specification and directions of the Engineer in charge.	Sqm	1382.48	1382.48	100	16-09-21	18-09-21	2
12	Excavation for roadwork in all types of soil by mechanical means including cutting and loading to tippers, trimming bottom and side slopes, in accordance with requirements of lines, grades and cross sections, and transportation with a lead of 1.00 km and complete as per specifications MORTH Specificatio MORTH Specification No.301Loading and unloading with 5ton loadcomplete as per specification and	Cum	3869.17	3869.17	100	11-09-21	15-09-21	4

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	: Executive Engineer Yelahanka Division
Project Name	: Comprehensive Development of Roads and Drains at Kaveri Layout, AMS Layout, Aditya Nagara 1st and 2nd stage Doddabettahalli, Yelahanka 4th Phase and Muneshwara Layout and Surrounding Areas in Ward No 93 of Yelahanka Division (Package No 12)
Consultants	: Civil Pro
Project Manager /Team Leader	: Karthik Rechan
Project Start Date	: 12-08-21
Project End Date	: 08-02-22
Project Length in Months	: 180 Days

Sl. No	Assignment	Unit	Modified schedule-B Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
13	Scarifying bitaminous course 50mm to 75mm thick along with premix carpet / surface dressing by road roller attached with scarifier without disturbing the base and stacking the debris including cost of all labour charges, HOM of machineries complete as per specification and directions of the Engineer in charge.	Sqm	1086.40	1086.40	100	11-09-21	13-09-21	2
14	Compaction of original ground by mechanical means including filling in depression occuring during rolling including cost of all labour, HOM complete as per specification and directions of the Engineer in charge.	Sqm	9230.89	9230.89	100	14-09-21	17-09-21	3
15	Construction of granular sub-base Grading-V as Sub-base and drainage layer by providing course graded crushed stone aggregates of granite/ trap/basalt material, mixing in a mechanical mix plant at OMC, Carriage of mixed material to work site, spreading in uniform layers with motor grader on prepared surface and compacting with vibratory power roller to achieve the 98 % proctor density, complete as per specifications Clause 401 of MORTH V Revision.complete as per specification and directions of the Engineer in charge.	Cum	1478.45	1478.45	100	18-09-21	21-09-21	3
16	Providing, laying, spreading and compacting cushed stone aggregates of granite / trap / basalt to wet mix macadam specifications including pre mixing the material with water at OMC in mechanical mix plant carriage of mixed materials by tipper to site, laying in uniform layers with paver in sub-base/base course on well prepared surface and compacting with vibratory roller to achieve the desired density complete as per specification and directions of the Engineer in charge.	Cum	1929.65	1929.65	100	22-09-21	24-09-21	2
17	Cleaning the existing WBM Road surface including removing of binding materials and other foreign matter with wire brushes and small picks sweeping with brooms or soft brushes and finally dusting with old gunny bags and bur or compressed air to receive bituminous treatment including cost of all materials, labbour, HOM of machineriescomplete as per specification and directions of the Engineer in charge.	Sqm	8389.80	8389.80	100	25-09-21	26-09-21	1
18	Providing and applying primer coat with S.S. bitumen emulsion on prepared surface of granular base such as WMM including cleaning of road surface and spraying primer at the rate of 0.60 kg / sqm using mechanical means complete as per specifications Clause 502 of MORTH V revision complete as per specification and directions of the Engineer in charge.	Sqm	491.38	491.38	100	27-09-21	29-09-21	2

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Comprehensive Development of Roads and Drains at Kaveri Layout, AMS Layout, Aditya Nagara 1st and 2nd stage Doddabettahalli, Yelahanka 4th Phase and Muneshwara Layout and Surrounding Areas in Ward No 03 of Yelahanka Division (Package No 12)
Consultants	:	Civil Pro
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	12-08-21
Project End Date	:	08-02-22
Project Length in Months	:	180 Days

Sl. No	Assignment	Units	Modified schedule-B Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
19	Providing and laying dense graded bituminous macadam using crushed aggregates of specified grading, premixed with VG30 grade bituminous binder and, transporting the hot mix to work site, laying to the required grade, level and alignment, rolling with smooth wheeled, vibratory and tandem rollers to achieve the desired compaction in all respects complete as per specifications Clause 505 of MORTH V revisionusing 40/60 TPH capacity H.M.P with Mechanical paver Gr-II (50 mm to 75 mm) with 4.5 % VG-30 Bitumencomplete as per specification and directions of the Engineer in charge	Cum	491.38	491.38	100	27-09-21	29-09-21	2
20	Cleaning the existing black topped surface with brooms,soft brushes and finally dusting with old gunny bags and/or compressed air to receive bituminous treatment including cost of all materials,labbour, HOM of machineries complete as per specification and directions of the Engineer in charge.	Sqm	14279.39	14279.39	100	30-09-21	01-10-21	1
21	Providing and applying tack coat using 80/100 grade bitumen(VG10) on the prepared black topped surfaces at 2.5 kg per 10 sqm, heating bitumen in boiler fitted with spray set (excluding cleaning of road surface) including cost of all materials, labour, HOM complete as per specification and directions of the Engineer in charge.	Sqm	14279.39	14279.39	100	02-10-21	04-10-21	2
22	Providing and laying bituminous concrete using crushed aggregates of specified grading, premixed with bituminous binder and filler, transporting the hot mix to work site, laying with a paver finisher to the required grade, level and alignment, rolling with smooth wheeled, vibratory and tandem rollers to achieve the desired compaction in all respects complete as per specifications Clause 507 of MORTH V revision using40/60 TPH capacity H.M.P. with Mechanical Paver Gr-II (30 mm to 45 mm) with 5.4% VG-30 Bitumencomplete as per specification and directions of the Engineer in charge.	Cum	571.18	571.18	100	02-10-21	04-10-21	2
23	Road Marking with Hot Applied Thermoplastic Compound with Reflectorising Glass Beads on Bituminous Surface/ Concrete Surface: Providing and laying of hot applied thermoplastic compound 2.5 mm thick including reflectorising glass beads at 250 gms per sqm area, thickness of 2.5 mm is exclusive of surface applied glass beads as per IRC:35 standards specified. The finished surface to be level, uniform and free from streaks and holes complete as per specification and directions of the Engineer in charge. QTY UPTO 125%	Sqm	559.70	559.70	100	04-10-21	05-10-21	1

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Comprehensive Development of Roads and Drains at Kaveri Layout, AMS Layout, Aditya Nagara 1st and 2nd stage Doddabettahalli, Yelahanka 4th Phase and Muneshwara Layout and Surrounding Areas in Ward No 03 of Yelahanka Division (Package No 12)
Consultants	:	Civil Pro
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	12-08-21
Project End Date	:	08-02-22
Project Length in Months	:	180 Days

Sl No	Assignment	Unit	Modified schedule-B Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
24	Dismantling of cement concrete pavement by mechanical means using pneumatic tools, breaking to pieces not exceeding 0.02 cum in volume and stock piling at designated locations and disposal of dismantled materials stacking serviceable and unserviceable materials seperately complete as per specification and directions of the Engineer in charge. QTY UPTO 125%	Cum	96.31	96.31	100	26-09-21	28-09-21	2
25	Cement concrete pavement.Construction of un-reinforced plain cement concrete pavement, using a grade concrete M30 over a prepared base with OPC coarse aggregate @ 0.69cum fine aggregate @ 0.46cum,coarse and fine aggregate confirming to IS-383-2016,with superplastisiser @3lts confirming to IS9103-2008mixed in a concrete mixer of not less than 0.6 cum capacity and appropriate weigh batcher as per approved mix design, laid in approved fixed side form work (steel channel, laying and fixing of 125 micron thick polythene film, wedges, steel plates including levelling the form work as per drawing). Spreading the concrete with shovels, rackers compacted using needle, screed and plate vibrator and finished in a continuous operation including provision of contraction, expansion, construction and longitudinal joints	Cum	415.93	415.93	100	28-09-21	03-10-21	5

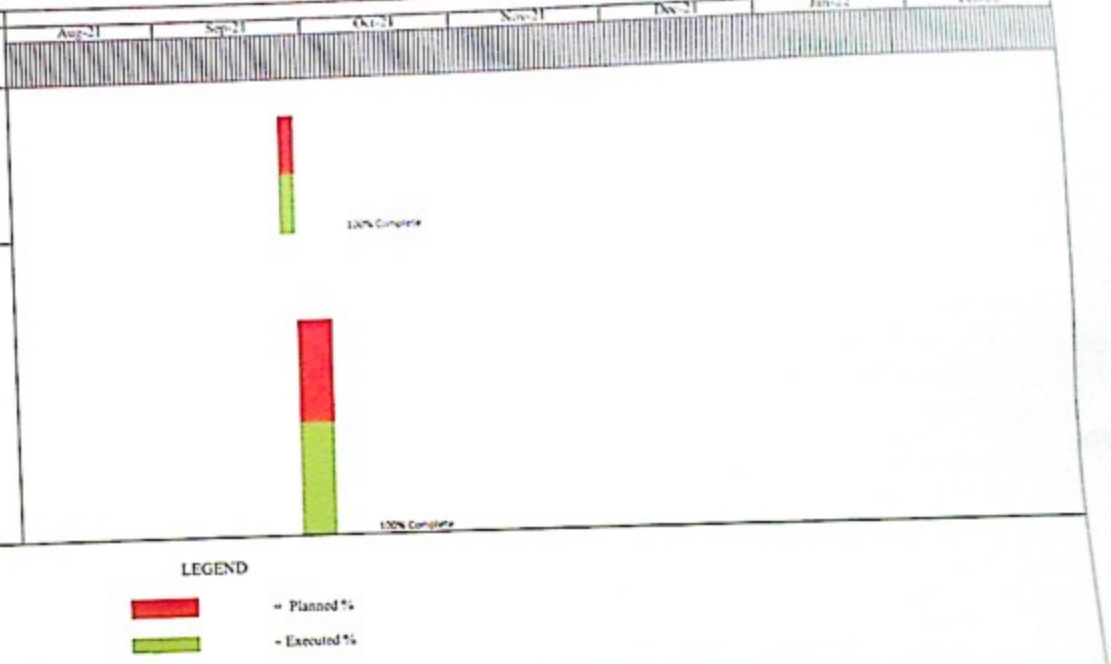

W-03 AE

AEE, YNT
